VTrans Working to Get You There
Vermont Agency of Transportation

Route Log Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Unit with questions or concerns.

DISTRICT	TOWN	ROUTE
7	CONCORD	US-2

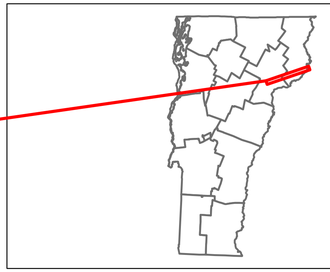

Base Map

1 in = 1.25 miles



Stick Diagram

- Primary Structures
- Secondary Structures
- Stations (Feet)
- Divided State Highway
- State Highway
- Divided Class 1 Town Highway
- Class 1 Town Highway
- Railroad Crossings
- District Boundaries
- Village/UC Boundary
- Town Boundary
- Ghost Section Boundary
- State/Town Highway Change
- Divided Highway Limits
- StreamCrossings Events

Scale:1in = 2000 FEET

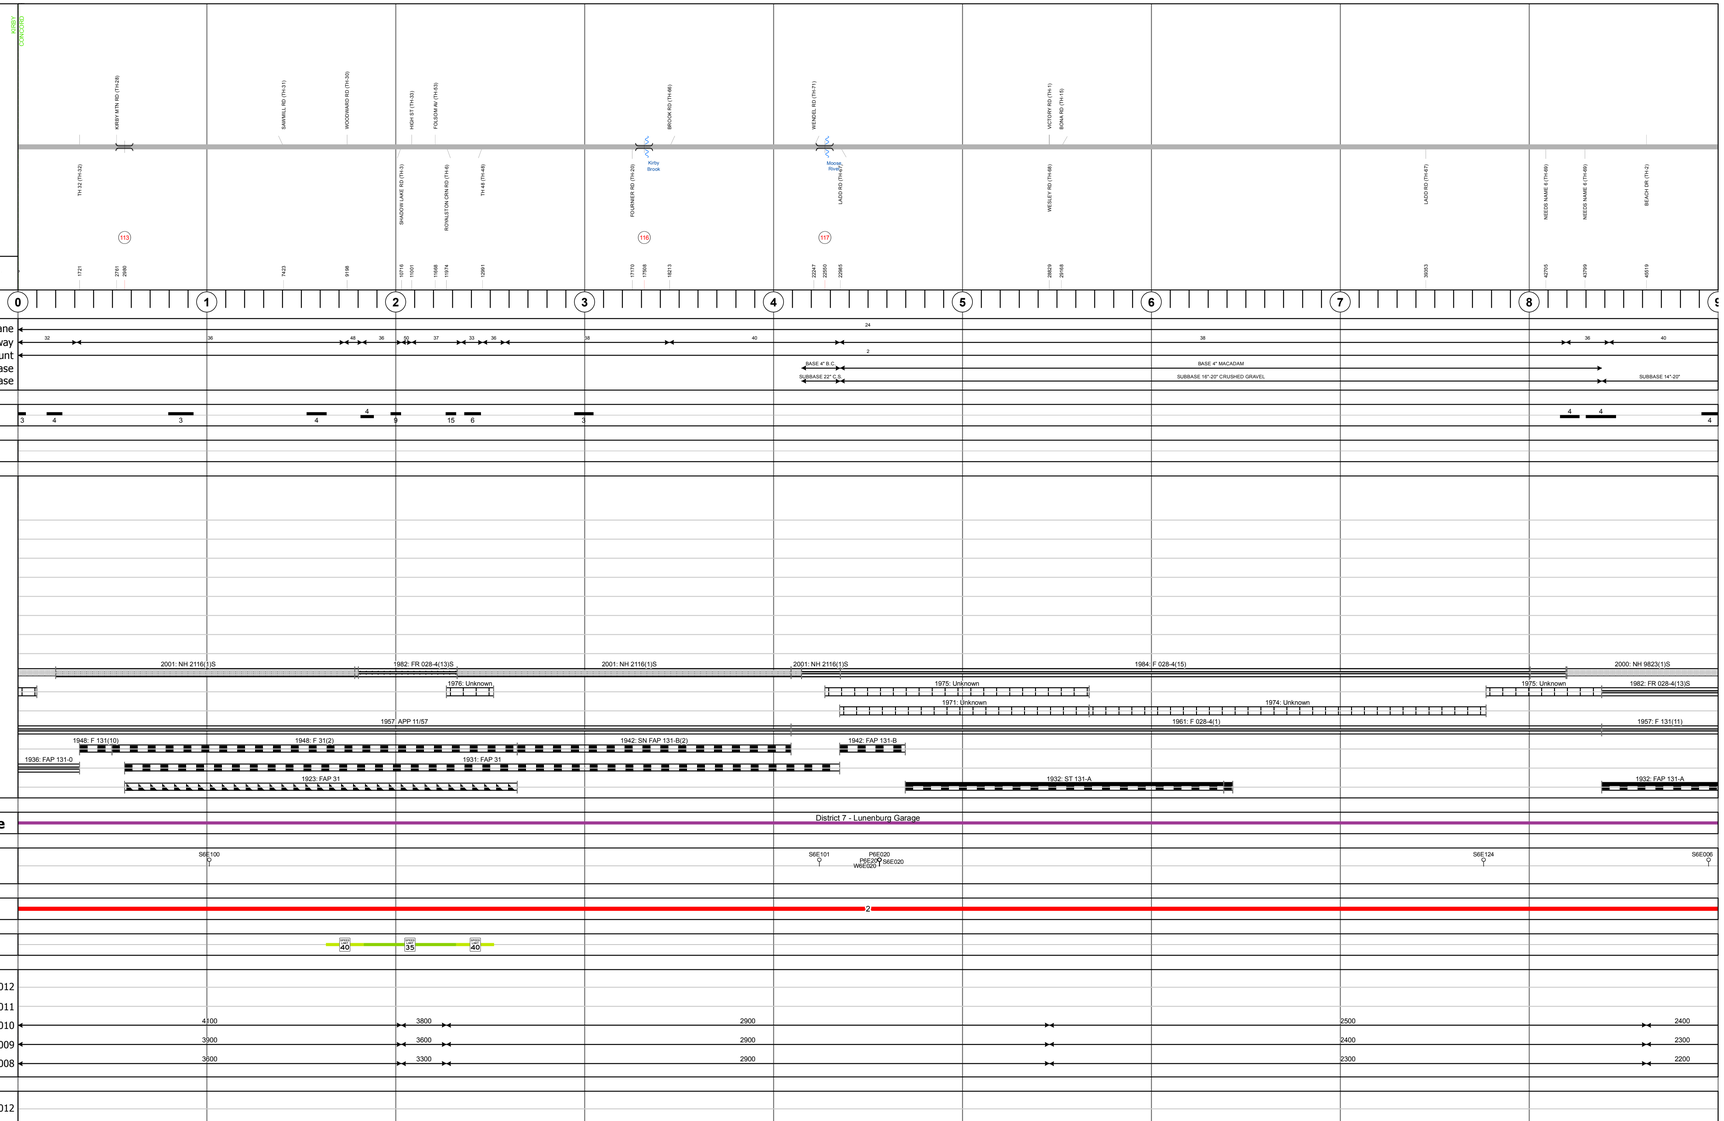

Road Widths



Curves

Grades



Historic Projects

Maintenance Garage

Traffic Counters

Functional Class

Speed Zone

AADT Counts

Crash Locations

DESCRIPTION BLOCK

Bridge No. 113: Culvert - 1933
Structure No. 30002801130S071
Length: 10'Under Clearance: 6.0'
Facility Carried: US2
Bridge Type: RC BOX CULVERT
Features Intersected: BROOK
Maintenance: State

Bridge No. 116: Culvert - 1942
Structure No. 30002801160S072
Length: 21'Facility Carried: US 00002 ML
Bridge Type: RC BOX
Features Intersected: KIRBY BROOK
Maintenance/Ownership: State

Bridge No. 117: Stringer/multi-beam or girder - 1961
Structure No. 30002801170S072
Length: 240', Width: 33.5'
Facility Carried: US 00002 ML
Bridge Type: 3 SPN CONT ROLLED BM
Features Intersected: MOOSE RIVER
Surface: Bituminous
Maintenance/Ownership: State

Historic Projects
Unknown; Bituminous Mix; Skinny Mix; Bituminous Seal; Bituminous Concrete; Bituminous Macadam; Cold Plane and Bituminous Concrete; Concrete; Gravel; Surface Treated Gravel; Plant Mix; Reclaimed Base and Bituminous Concrete

Functional Class
1 7 12 17
2 8 14 19
6 11 16

Speed Zones
SPEED LIMIT 25 30 35 40 45 50 55 60 65

Curves
curve left
curve right

Grades
grade up
grade down

Traffic Counters
(counter ID)

Road Widths
(ft)

AADT
(count)

Crash Locations
Fatal; Injury; Property Damage Only; Unknown Crash Type

Mileage by Functional Class By Sheet

028-4	2 - Rural - Principal Arterial	9.0

Total Mileage: 9.0 mi

Mileage by Town By Sheet

CONCORD - U002-0507		9.0 of 10.765

Total Mileage: 9.0 mi

DISTRICT	TOWN	1 of 2 mile 0.0 to mile 9.0	ROUTE
7	CONCORD	Date: 04/08/13	US-2
