Route Log Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Unit with questions or concerns.

DISTRICT	TOWN	ROUTE
1	LANDGROVE	VT-11

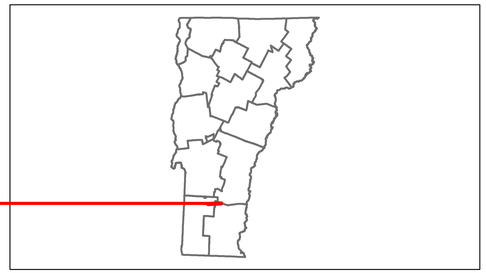

Base Map

N

1 in = 2,000 feet

Stick Diagram

Road Widths

Travellane	36
Roadway	42
Lane Count	2
Base	
Subbase	

Curves

3, 4, 4, 3

Grades

-9.0, +6.6 A +5.8

Historic Projects

1993: STP 9354(11)S
1984: F 016-1(11)
1976: Unknown
1948: F 93(11)

Maintenance Garage

District 2 - Londonderry Garage

Traffic Counters

Functional Class

6

Speed Zone

AADT Counts

2012	3800
2011	3800
2010	3700
2009	3700
2008	3600

Crash Locations

2012
2011
2010
2009
2008

DESCRIPTION BLOCK

Bridge 22:
Tee Beam - 1926
Structure No. 200016002202052
Length: 25'
Width: 29.4'
Facility Carried: VT 00011 ML
Bridge Type: CONCRETE T-BEAM
Features Intersected: FLOOD BROOK
Surface: Bituminous
Maintenance/Ownership: State

Historic Projects

Retreatment
Resurface
Unknown
Bituminous Mix
Skinny Mix
Bituminous Seal
Bituminous Concrete
Bituminous Macadam
Cold Plane and Bituminous Concrete
Concrete
Gravel
Surface Treated Gravel
Plant Mix
Reclaimed Base and Bituminous Concrete

Functional Class

1, 7, 12, 17, 2, 8, 14, 19, 6, 11, 16

Speed Zones

SPEED LIMIT 25, 30, 35, 40, 45, 50, 55, 60, 65

Curves

curve left
curve right

Grades

grade up
grade down

Road Widths

(ft)

Traffic Counters

(counter ID)

AADT

(count)

Crash Locations

Fatal
Injury
Property Damage Only
Unknown Crash Type

Mileage by Functional Class By Sheet

016-1	6 - Rural - Minor Arterial	0.821

Total Mileage: 0.821 mi

Mileage by Town By Sheet

LANDGROVE - V011-0205	0.821 of 0.821

Total Mileage: 0.821 mi

DISTRICT	TOWN	Date: 11/15/13	ROUTE
1	LANDGROVE	1 of 1 TWN mileage: 0.0 to 0.821	VT-11 ETE mileage: 12.012 to 12.833
